



Wa-Hi

- Building 5, North area cabinet install, painting, grid ceiling installation, flooring prep, beginning of electrical/lighting installation. West area room finish including flooring, painting, white boards and short throw projection installation. East area finish work including lighting installation and power up, painting, tile work, finish plumbing, finish electrical, flooring. South area installation and power up of lighting, glazing installation and other trim and finish work throughout. Mezzanine level IDF room finishing started, fiber pull throughout the entire project, electrical and mechanical finishing installation and preparing for start up and commissioning.
- Building 7 (Auditorium) Black box theater and green room punch list items being worked on. Exterior of the building soffits installed and prepped for painting.
- Building 6 Main entry area painted and prepped for FRP installation. 60's locker rooms, locker bases installed, tile installed, lighting installed, mechanical and plumbing rough in continues. 90's locker rooms demo completed, slab cuts and underground plumbing installed and slab poured back into place, framing was installed and electrical and plumbing rough in started. ROTC and health classroom, east and west upper floor areas were moved out of by the district and abatement work began in these areas.
- Building 1 greenhouse abatement work continued, classrooms were moved out of and demolition work began. Pre engineered metal building painted, and lighting and fire sprinklers were installed.
- Parking lot 3 was paved and striped. Parking lot 4 was finished graded final prep for paving began.
- Work on new bulb outs and drainage on Abbott Rd started work.
- Portable offices and modulars at building 8 and 1 were dismantled and removed with the district keeping 2 modular that were stored at the Paine street warehouse.
- Landscaping work including underground water main was installed throughout the project area.
- The design team worked with Jackson to complete and return submittals and answer construction questions as they arose in order to facilitate that the project continues to be able to keep up with the schedule.
- Across the site, Jackson continued to move fences and provide pathways to ensure campus and student safety.
- Wenaha, Jackson, and the School district worked on coordinating efforts to ensure the upcoming phases can be initiated while also accommodating staff and moving activities for next remodel/update activities.

Pioneer Middle School

- In Area 6 Science and Art classrooms, work continued this month with mechanical trades finishing rough in and insulation and drywall following.
- CTE room received new sound panels giving the CMU walls added sound dampening.
- At the exterior siding work continues all around the building.
- Area 6 roof had new shingles being installed with roof work continuing into July.
- At Roosevelt Street a new storm drain catch basin was installed and preparation for new sidewalks began.

June 2022 Project Update



- SEATech students worked hard to get the roof sheeting on the new Track storage shed before school was out. Jackson Construction will complete the balance of work needed to finish the shed project this summer.
- The old north portables demolition began this month. The structure will be completely removed, and the parking area expanded.
- Sports fields at west and east areas will begin topsoil and irrigation install in the coming month.
- Jackson Construction, Architects West and the WWPS team continue to coordinate to deliver a project WWPS can be proud of.

Lincoln High School

- In June the 3rd level hallway saw the old wood finish stripped off in preparation for new stain finish in early July.
- New HVAC units arrived and were installed on roof.
- The 2nd level elevator vestibule open to the Commons area had the metal handrail installed and painted.
- On the 1st level, the hallway received the epoxy floor finish and base trim at south end of hall.
- At the exterior of building, more windows, doors, and louvers continue to be installed.
- The existing portable classroom demolition began, in preparation for the new parking lot.
- Curbing and sidewalks were installed around the building.
- WWPS, Wenaha, Architects West and Chervenell continue to work together to finish this great remodel in time for school this Fall.



Attachment A: Wa-Hi Progress Photos



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update





Attachment B: Pioneer Progress Photos



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update





Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update






Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update





Attachment C: Lincoln HS Progress Photos

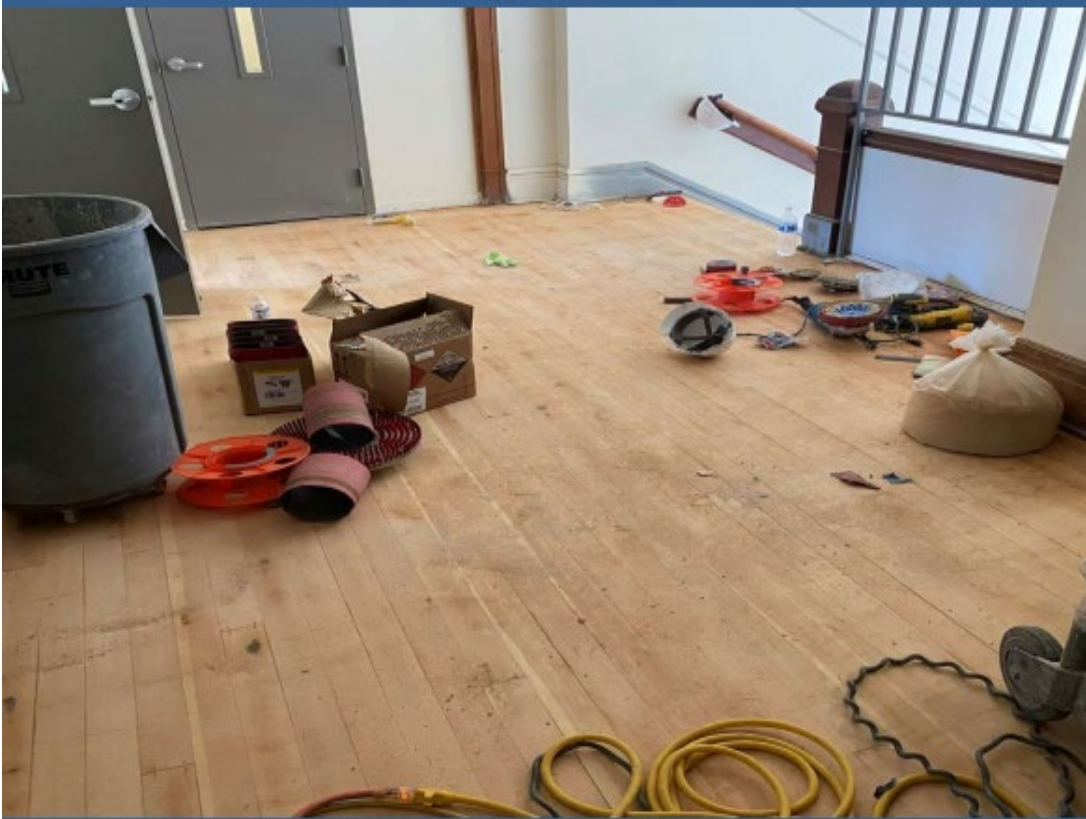

Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update





Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update



Walla Walla Public Schools - 2018 Bond Project
June 2022 Project Update

