Walla Walla Public Schools - 2018 Bond Project

September 2021 Project Update

Wa-Hi

- In Building 2 (Old Science) punch list items were worked on.
- Building 3 (Commons), drywall installation, HVAC install, electric rough in installation continued and, glass at the front of the building was installed. Kitchen area was framed, and drywall started. Large hood at the cooking line was installed.
- Building 4 (Library) was punch listed and punch list was worked on. Circulation desk was installed in the library. Culinary arts equipment was commissioned and furniture was installed.
- Building 5, Abatement continued in various areas. Demolition work in main floor and mezzanine work was on going in various areas. Saw cutting of the floor in preparation for underground plumbing was installed. Installation of the underground plumbing and electrical was started.
- Building 6 (Gym) was punch listed and the punch list was worked on. Work on the lobby was continued. Weights and fitness classes began using the space. The athletic flooring for this area is on backorder and expected to arrive in late October.
- Building 7 (Auditorium) new carpet was laid in the auditorium and lobby, demolition of the existing music rooms was initiated along with abatement work. Punch list work continued in the new addition.
- The parking lot near the gym continued including the demolition of the old fitness building, rough grading and set up for curbing was done. Preparation for the walkway up to the pedestrian bridge. Addition of dry wells and other underground services were added. Crushing of the recycled asphalt was completed.
- Seating wall in courtyard was formed and poured.
- The new pedestrian bridge railing was repainted.
- The design team worked with Jackson to complete and return submittals and answer construction question as they arose in order to facilitate that the project continues to be able to keep up with the schedule.
- Across the site, Jackson continued to move fences and provide pathways to ensure campus and student safety.
- Wenaha, Jackson, and the School district worked on coordinating efforts to ensure the summer phases can be initiated while also accommodate staff and moving activities out for next school year's remodel/update.

Pioneer

- North classroom remodel wrapped up and students were welcomed back to school. Fresh paint, new flooring, lighting, cabinets, and new restrooms. Fire suppression system came online as well. Updates to data, projectors and HVAC were also a big part of the classroom remodel.
- Administration area 5, ceiling grid and data cable was installed.
- New entry area restrooms, student store drywall and ceramic tile installed.
- Aux gym, mechanical ducts and rain drains went in. Acoustical panels were installed and painted.
- Kitchen saw the cooler and freezer units installed, drywall began, and kitchen vent hood was hung.
- Music room's interior framing was installed. Restrooms in this area continued plumbing rough in.

- Main Gym, Drywall installed in gym and locker room areas. Acoustical panels began.
- Area 1 classroom finishes began with paint and ceiling grid install.
- Site work this month included sidewalks installed at west side Bridge St. and excavation at south side of structure for new loading dock and underground electrical for new light poles along service road and south parking area.

Lincoln

- Chervenell Construction mobilized, set up jobsite, and installed fencing.
- Selective demolition began on all three levels of structure as required.
- Site work included tree removal and install of water service vault near entrance at 4th Street.
- A walk-path for students was installed from 3rd Street for safe access to portables.

September 2021 Project Update

Attachment A: Wa-Hi Progress Photos

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

September 2021 Project Update

Attachment B: Pioneer Progress Photos

September 2021 Project Update

Genie GS-2646
9/16/21, 10:01 AM

9/28/21, 9:51 AM

September 2021 Project Update

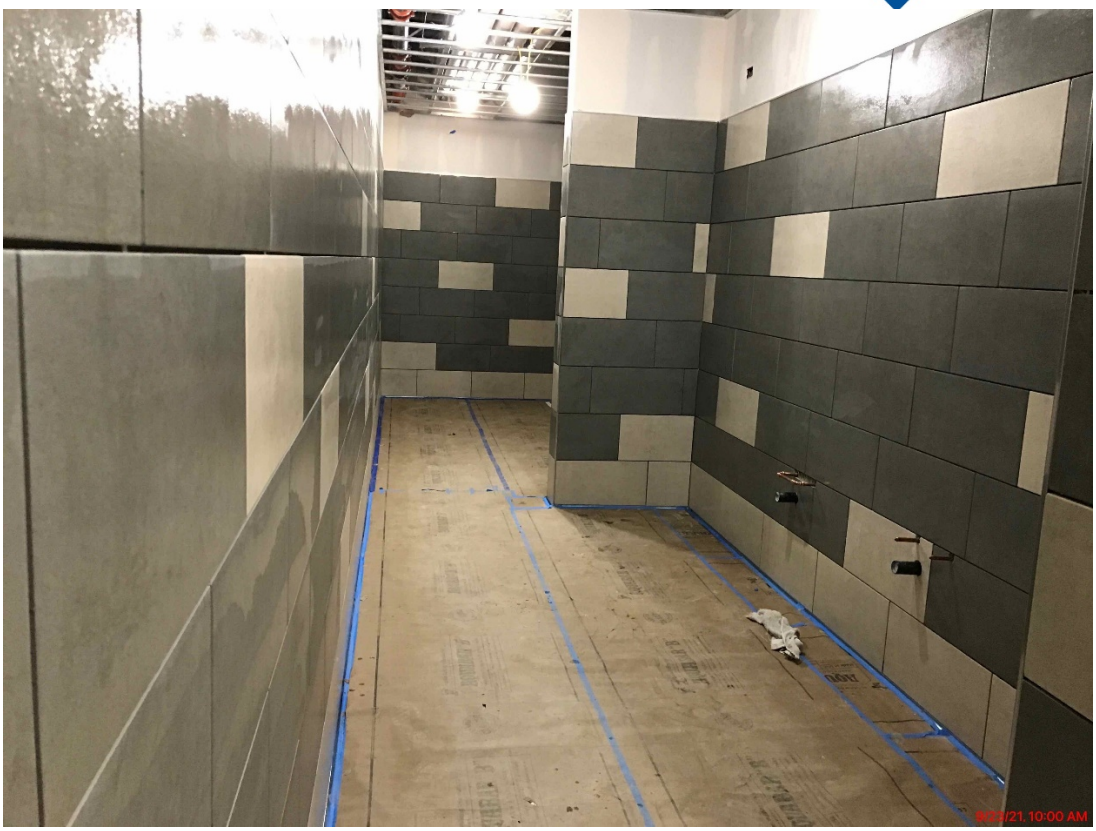

September 2021 Project Update

September 2021 Project Update

Attachment C: Lincoln HS Progress Photos

September 2021 Project Update

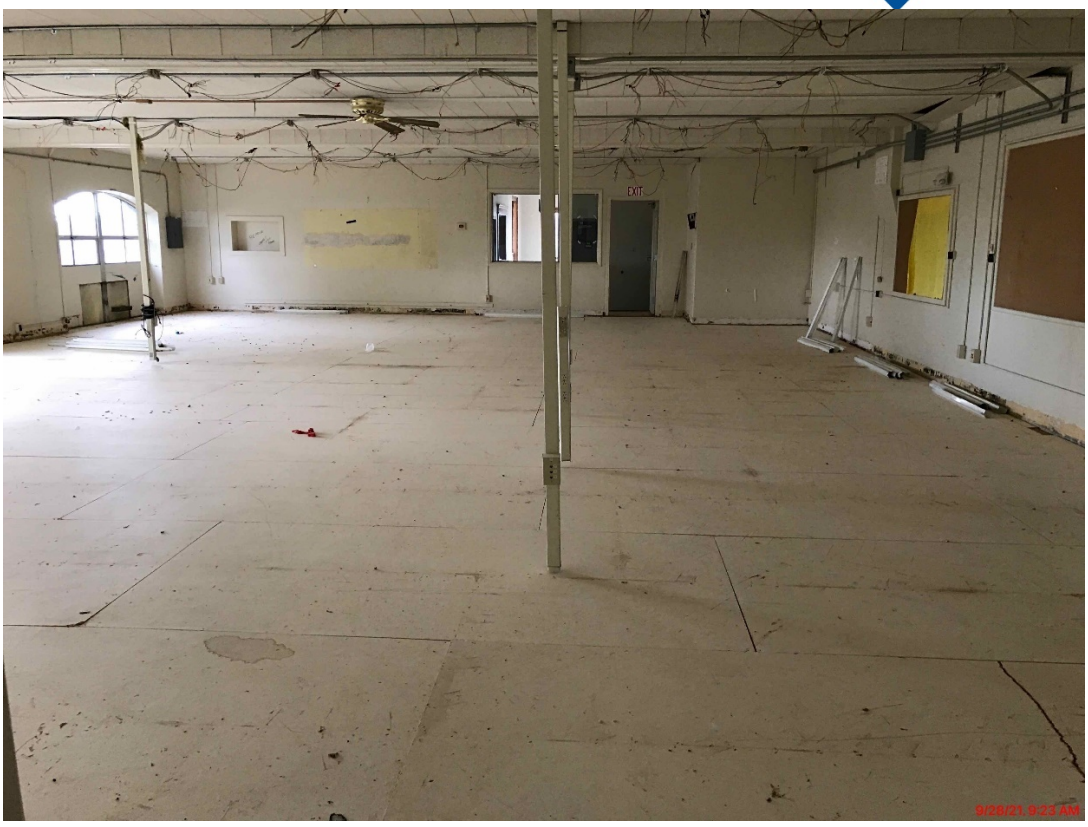

September 2021 Project Update

September 2021 Project Update
